




## Syncrude Development - Stage 3 Expansion



Aurora Trucks Dump into Crusher

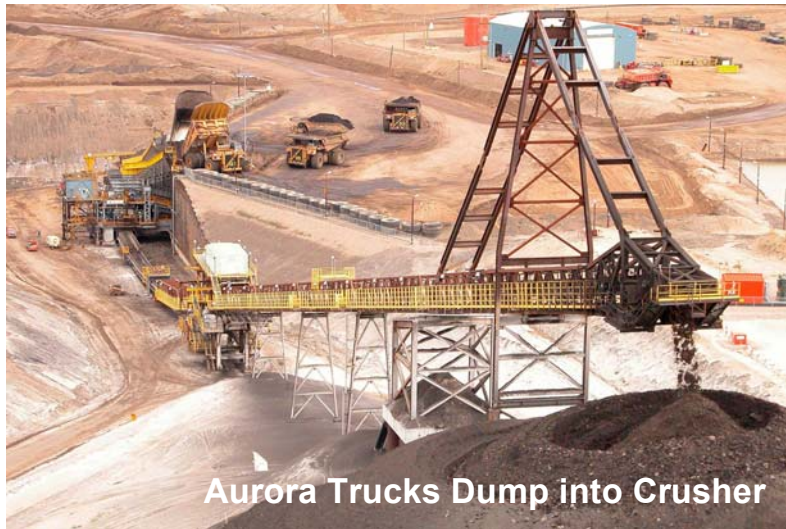

Upgrader Expansion

- **Expand production by 50%**
  - Upgrade total site quality
- **\$7.8 billion total project**
  - New mine (\$0.7 G)
  - Upgrader expansion (\$7.1 G)
- **Mine complete**
  - On budget, on schedule
- **Upgrader 50% complete**
  - Disappointing cost/schedule performance
  - Intervention steps implemented
  - 2006 start-up
